



2019 Bond



Jacobs

# Tarrant County College District

## 2019 Bond Capital Improvements Program

Bond Report 13  
April 2022



## Executive Summary


The 2019 Bond Program is moving forward on schedule. Construction continues on the two largest components – the Northwest Campus Redevelopment and the Southeast Campus Renovation and Expansion – and progress continues on the Construction Documents phase of design for the renovations scope for the Southeast Campus. Additionally, early projects within the MEP Infrastructure (MEP) and 3 Goals and 8 Principles (3G8P) programs are underway. A total of 129 projects are scheduled in the \$919 million program with \$258.7 million (28.2% of program) committed and \$133.6 million (14.5% of program) spent to date.

The Northwest Campus Redevelopment construction progress continues with construction of the exterior building envelope and interior mechanical, electrical, and plumbing components progressing in Buildings 1 and 2. At the Southeast Campus Renovation and Expansion project, relocation of existing utilities is underway. Behind the scenes, planning for upcoming renovation work continues, including swing space, furnishings, and logistics.

The Bond Team continues to track the volatile construction market and its impact on project costs and material delivery times. The emphasis continues to be on a constant drive for best value through diligent cost control and schedule management.

Following are highlights of the major projects and initiatives:

### Northwest Campus Redevelopment

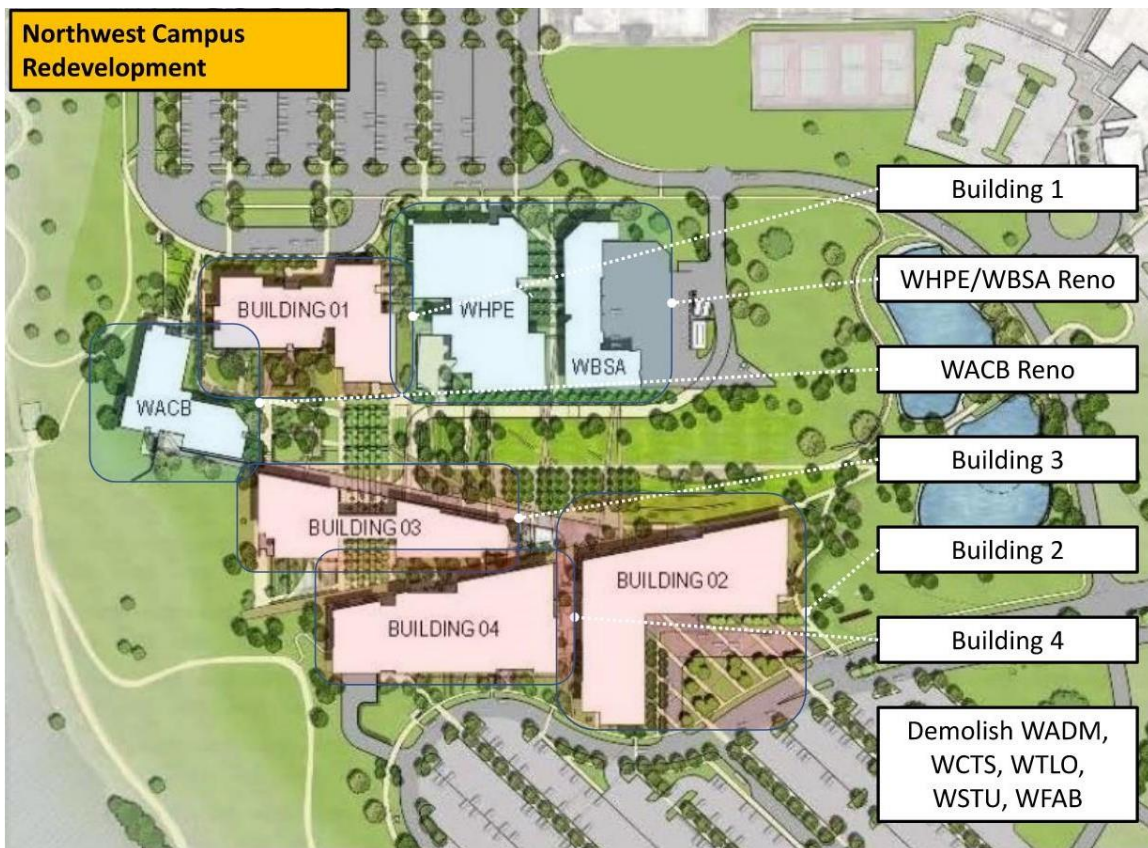

Construction progress in March for Buildings 1 and 2 by the Skanska USA Buildings Inc (Skanska) construction team continued to show positive major achievements. As Skanska targets the next major milestone to “dry-in” the new buildings, installation of roofing and waterproof siding has started. Skanska is also continuing with interior metal wall framing, mechanical and plumbing system installations, and rough-in of electrical systems. All slab on grade and elevated concrete slab work has been completed. Door frames are being installed and window frames and glass are tracking to begin in early April. The construction schedule continues to track on time, as expected, with rigorous



review to mitigate minor delays resulting from weather impacts and taking advantage of opportunities to make schedule gains through well thought out plans and contingencies.


The Construction Hub (pre-engineering metal building for the CMaR and TCCD construction teams) has been completed. Moving the CMaR and Bond Team construction teams will commence in the coming weeks which will free up additional parking for the Northwest Campus behind the WATB Building.

The Project Team completed development of an early Site Work package in February 2022 to complete selected critical path construction elements ahead of the last major construction package for Buildings NW02 and NW03. This early construction work will mitigate scheduling and phasing impacts to the Northwest Campus operations. This early Site Work package consists of renovations to the existing north and south parking lots, installation of site utilities (primary electrical ductbanks and storm drainage) under those parking lots, as well as parking lot lighting. Skanska posted the advertisement of this Site Work package to the subcontractor community and received bids in early March 2022. Skanska is tracking to deliver their GMP proposal to the Bond Team by the end of March 2022 and the Team expects to present the WA-1 Amendment to the CMaR Agreement for Skanska to the Board of Trustees for approval at the May 2022 Board meeting.

The Bond Team continues working with Campus leadership to mitigate potential operational disruptions or service outages. The next expected construction event with direct impacts to the Campus is the phasing of the work for renovations to the North and South Parking Lots. The Bond Team is coordinating closely with the Northwest Campus leadership team as well as the Campus Police Department to develop a phasing plan to mitigate traffic impacts.

The Bond Team and Huckabee Associates (Huckabee), the project Architect, continue to engage with the Real Estate and Facilities Department’s Interiors Design Group for procurement planning and budget management of Furniture, Fixtures, and Equipment, Audio-Visual Equipment, Information Technology Equipment, and Specialty Educational Equipment to clarify processing, coordination efforts, and future implementation of those processes and procedures into the design documents.

**Southeast Campus Renovation and Expansion**

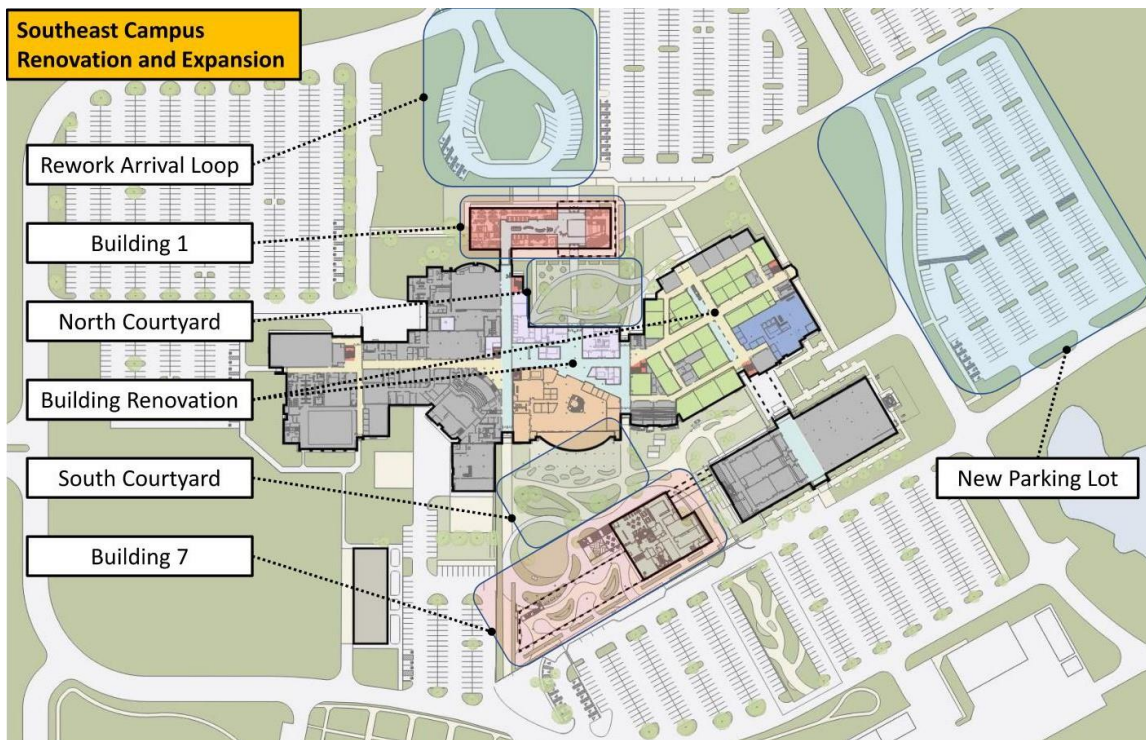

As a result of approval by the Board of Trustees in February 2022 and subsequent execution of the Work Authorization Number ONE (WA-1) Amendment to the Agreement with Byrne | Potere | Hunt, a Joint Venture (BPH)



as Construction Manager at Risk (CMaR), a Notice to Proceed with construction was issued for the Site Utilities Relocation and Long-Lead Structural Steel Procurement package. The BPH construction team has mobilized at the Southeast Campus and has been working to locate existing underground utilities and preparing for relocation of those utilities into their new alignment out of the footprint of the site for the two new Buildings 1 (North Student Onboarding) and 7 (South Academic). They have also released their subcontractor to begin the engineering process to develop submittals in preparation for placing the order for the long-lead structural steel.

On February 17, 2022, Perkins + Will issued the 80% Construction Documents GMP-1 package for the North Student Onboarding Building (Building 1), South Academic Building (Building 7), and site improvements to BPH for solicitation of bids through the subcontractor community to establish a Guaranteed Maximum Price ONE (GMP-1). Subcontractor bids were received by BPH on March 30, 2022, and are currently underway with the evaluation process and conducting post-bid interviews in anticipation for submitting the GMP-1 package to the Bond Team for thorough analysis and negotiations. Subsequent to negotiations, the Bond Team anticipates presenting the GMP-1 Amendment to the CMaR Agreement with BPH for consideration and approval by the TCCD Board of Trustees on May 19, 2022.

Now that Perkins & Will, Inc. (P&W), as project Architect, has completed the construction document set for Buildings 1 and 7, they can focus on finishing the design process to deliver the construction document set for the existing building renovations. P&W is tracking to start this final phase of design in March 2022 and complete the construction document set in July 2022.

The Project Team continues planning for commencement of the existing building renovations in 2024. After careful analysis and review of various swing space and remote learning options, the TCCD leadership selected "Option 1B" which provides temporary workstations in the existing building gymnasium and ballroom, then starts and finishes all renovations in the 2024 calendar year. This plan was presented to the Board of Trustees at the March 10, 2022, meeting as part of the Quarterly Bond Capital Improvements Program Update.

BPH continues to provide preconstruction services such as cost estimating for the remainder of the project construction phases, schedule development support, and project-related permitting conversations with the City of Arlington as the Building Code Official. With the commitment of funding for the WA-1 package, BPH provided an update to the project construction estimate based on the 50% Construction Document set for Buildings 1 and 7 and the 100% Design Development set for the existing building renovations. The results showed a continued escalation in the cost of construction resulting primarily from a variety of volatile market factors including escalation, inflationary pressure, labor shortages, commodity and material shortages, and increased material and equipment delivery timelines.

P&W and the Bond Team continue to engage with the Real Estate and Facilities Department's Interiors Design Group for procurement planning and budget management of Furniture, Fixtures, and Equipment, Audio-Visual Equipment, Information Technology Equipment, Emergency Alert Systems, and Specialty Educational Equipment to clarify processing, coordination efforts, and future implementation of those processes and procedures into the design documents.

The Bond Team is also working towards development of a procurement package and scope of services for a Move Management consultant and a Moving Services provider in preparation for the various moves that are planned to occur in early calendar year 2024 with the completion of construction of Buildings 1 and 7 and ahead of the existing building renovations.

### **3 Goals and 8 Principles (3G8P) and MEP Infrastructure Programs**

The Bond Team continues work a variety of 3G8P and MEP Infrastructure projects (16 in the active status and 9 in closeout) that will not be directly affected by the forthcoming Master Implementation Planning efforts being performed by Corgan. These projects include the 2021 IILE Classroom Renovations; 2022 IILE Classroom Renovations; and the District-Wide Emergency Power System Upgrades, as well as the planning and execution of several MEP Infrastructure upgrades across the District.



New projects under these two Programs, which have recently begun, include the 2022 IILE Classroom Renovations at the Northeast Campus NTAB building and South Campus SACB and SACD buildings (advertisement to solicit bids has been posted by the Procurement Department), District-Wide Emergency Power System Upgrades (scoping and planning phase), and the Southeast Campus Chiller Upgrades (construction underway.)

The Bond Team continues coordination with the TCCD Real Estate and Facilities Department's Executive Director for Strategic and Institutional Planning for the Master Implementation Planning effort. This effort will address existing facilities at the Northeast, South, Trinity River, and Alliance at Northwest Campuses, as well as the remaining portions of the existing Northwest and Southeast Campuses that have not undergone the master planning process. The contract for these services was approved by the Board of Trustees at the October 2021 meeting to be performed by Corgan.

### **M/WBE & HUB Outreach**

The Bond Team continues to maintain a highly visible presence in the M/WBE contracting community. On March 2 the Southeast Campus Renovation & Expansion project team held a successful MWBE Outreach event at the campus. On March 16 the Bond Team was invited to speak at a webinar sponsored by the Fort Worth Hispanic Chamber of Commerce, to present upcoming bidding opportunities in the program. The team participated in a total of 16 events in March, with another six planned so far for April.

For the fiscal year to date, the M/WBE spend for the Bond program is \$4,869,674 for construction, including special trades, (30.3% of construction spend versus the goal of 27.0%) and \$1,204,951 for professional services (33.5% of professional services versus the goal of 23.7%). These metrics will be tracked and managed for the duration of the bond program.

Upcoming Board Presentations and Bond Management Team Action Items:

- In April:
  - 3 Goals and 8 Principles Program: Standard form of Agreement between Owner and Contractor for Americans with Disabilities Act (ADA)/Texas Department of Licensing and Regulation (TDLR) Improvements for the Bond-Funded FY-21 District-Wide IILE Classroom Renovations, for Board approval.
  - Mechanical, Electrical, Plumbing/Infrastructure Program: Standard form of Agreement Between Owner and Contractor Agreement for Northeast Campus Sewer Rehabilitation, for Board approval.
- In May:
  - Southeast Campus Renovation and Expansion: Guaranteed Maximum Price ONE (GMP-1) Amendment with Construction Manager at Risk (Byrne | Potere | Hunt, a Joint Venture) for construction of new Buildings 1 and 7, for Board approval.
  - Northwest Campus Redevelopment: Work Authorization ONE (WA-1) Amendment with Construction Manager at Risk (Skanska USA Buildings Inc.) for North and South Parking Lot Renovations and Associated Site Work, for Board approval.
  - 3 Goals and 8 Principles: Standard form of Agreement Between Owner and Contractor for Bond-Funded FY-22 IILE Classroom Renovations (Buildings NTAB, SCAB, and SCAD)
- In June:
  - Quarterly Report of the 2019 Bond Capital Improvements Program status through May 2022, for Board information

### **Attachments**


Attached to this report is the Program Summary Report and Individual Project Reports.




# Financial Summary Report

Report Date: 3/28/2022

Budget by Bucket

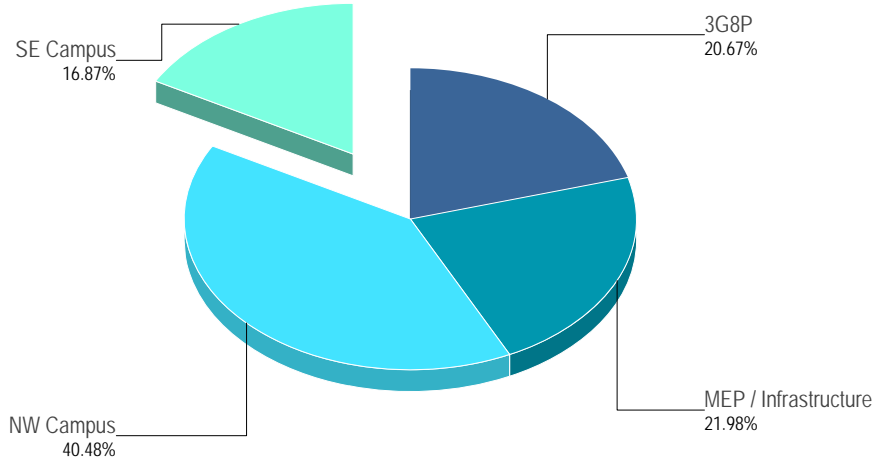

Budget by Campus

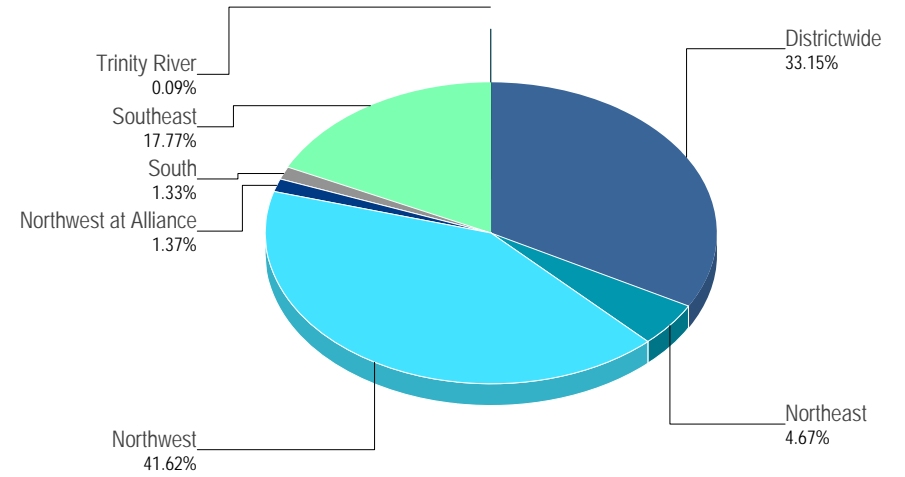

Description	Campus	BUDGET		COST COMMITMENTS			EXPENDITURES			
		A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
		Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended

**Fund 90**

**NW Campus**

Northwest VB Campus Re-Development	Northwest	308,000,000	161,444,788	-657,704	160,787,084	0	160,787,084	147,212,916	70,492,998	22.89%
<b>Total for NW Campus :</b>		<b>308,000,000</b>	<b>161,444,788</b>	<b>-657,704</b>	<b>160,787,084</b>	<b>0</b>	<b>160,787,084</b>	<b>147,212,916</b>	<b>70,492,998</b>	<b>22.89%</b>

**SE Campus**

Southeast Campus Expansion	Southeast	125,000,000	15,790,149	6,644,265	22,434,414	0	22,434,414	102,565,586	6,295,878	5.04%
<b>Total for SE Campus :</b>		<b>125,000,000</b>	<b>15,790,149</b>	<b>6,644,265</b>	<b>22,434,414</b>	<b>0</b>	<b>22,434,414</b>	<b>102,565,586</b>	<b>6,295,878</b>	<b>5.04%</b>

**3G8P**

Bucket - 3G8P Holding	Districtwide	147,478,684	0	0	0	0	0	147,478,684	0	0.00%
NTAB and SCAB/D Classrooms Renovations	Districtwide	10,202,128	699,250	0	699,250	0	699,250	9,502,878	0	0.00%
DT Bond Program Manager Firm - 3G8P	Districtwide	7,781,919	7,781,919	0	7,781,919	0	7,781,919	0	2,069,905	26.60%
DT VB Wayfinding Program	Districtwide	6,000,000	736,486	5,574	742,060	0	742,060	5,257,940	363,355	6.06%
DT VB IILE Classroom Renovation	Districtwide	5,153,702	4,602,678	-2,051	4,600,628	0	4,600,628	553,075	4,348,265	84.37%
OWTL Corporate Services Renovation	Northwest at Alliance	4,738,470	4,590,360	-243,841	4,346,520	0	4,346,520	391,950	4,346,520	91.73%

## Financial Summary Report

Description	Campus	BUDGET		COST COMMITMENTS				EXPENDITURES		
		A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
		Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
OWTL Welding Lab Expansion	Northwest at Alliance	4,404,841	4,395,626	-3,000	4,392,626	0	4,392,626	12,214	4,208,695	95.55%
SO STEC Welding Lab Expansion	South	3,365,579	3,501,607	-136,028	3,365,579	0	3,365,579	0	3,365,579	100.00%
SACD_1403_1406_1407_1411_21st Century Classroom Upgrades	South	456,837	467,973	-11,136	456,837	0	456,837	0	456,837	100.00%
WFSC_2603_2605_21st Century Classroom Upgrades	Northwest	231,351	249,597	-18,246	231,351	0	231,351	0	231,351	100.00%
ESEE 21st Century Classroom Upgrades	Southeast	143,830	147,732	-3,902	143,830	0	143,830	0	143,830	100.00%
SO SELE Building Renovation	South	42,660	42,660	0	42,660	0	42,660	0	42,660	100.00%
<b>Total for 3G8P :</b>		<b>190,000,000</b>	<b>27,215,888</b>	<b>-412,630</b>	<b>26,803,259</b>	<b>0</b>	<b>26,803,259</b>	<b>163,196,741</b>	<b>19,576,995</b>	<b>100.00%</b>

### MEP/Infrastructure

Bucket - MEP / Infrastructure Holding	Districtwide	120,758,272	0	0	0	0	0	120,758,272	0	0.00%
DT VB Generator Installation	Northeast	35,091,000	0	0	0	0	0	35,091,000	0	0.00%
DT Bond Program Manager Firm - MEP	Districtwide	6,306,635	6,306,635	0	6,306,635	0	6,306,635	0	1,677,495	26.60%
NW VB Power Installation	Northwest	4,886,367	4,877,371	-109,907	4,767,464	0	4,767,464	118,903	4,713,600	96.46%
NW WBSP Chiller/Cooling Towers Replacement	Northwest	3,448,393	3,378,426	-32,407	3,346,019	0	3,346,019	102,374	3,340,583	96.87%
SE EBSP Cooling Tower Replacement	Southeast	2,795,126	2,902,392	-107,266	2,795,126	0	2,795,126	0	2,795,126	100.00%
SE EBSP Chiller Replacement	Southeast	2,598,305	2,700,126	-968,000	1,732,126	0	1,732,126	866,180	68,775	2.65%
SO VB UPS and Generator Installation	South	2,552,065	2,583,424	-44,275	2,539,149	0	2,539,149	12,916	2,326,444	91.16%
Chiller Replacement	Northeast	2,535,612	2,546,074	-10,462	2,535,612	0	2,535,612	0	2,535,612	100.00%
NE VB Sewer Rehabilitation	Northeast	2,528,500	2,486,273	-58,274	2,427,998	0	2,427,998	100,502	1,005,640	39.77%
OWTL AHU/VAV Replacements – Phase II: 1st and 2nd Floor 91 Section	Northwest at Alliance	2,176,972	2,225,574	-48,603	2,176,972	0	2,176,972	0	2,176,972	100.00%
NE NBSP Boiler Replacement	Northeast	1,700,161	1,743,475	-43,779	1,699,696	0	1,699,696	465	1,699,696	99.97%
SE VB Generator Installation	Southeast	1,543,930	1,551,682	-67,224	1,484,457	0	1,484,457	59,473	1,418,816	91.90%
Sanitary Sewer Rehabilitation Phase II	South	1,441,621	1,497,300	-55,680	1,441,621	0	1,441,621	0	1,441,621	100.00%
OWTL Air Handler Replacement	Northwest at Alliance	1,260,282	1,312,359	-52,078	1,260,282	0	1,260,282	0	1,260,282	100.00%
SE VB UPS and Generator Installation	Southeast	1,102,878	1,114,576	-48,934	1,065,641	0	1,065,641	37,237	1,057,738	95.91%
SAUT & SACR Fire Sprinkler Upgrades	South	672,370	877,925	-205,555	672,370	0	672,370	0	672,370	100.00%
SO SPAC Lighting Installation	South	651,357	651,357	-55,224	596,134	0	596,134	55,224	594,141	91.22%
TR VB Power Installation	Trinity River	628,498	628,498	-40,000	588,498	0	588,498	40,000	504,678	80.30%
NW WFSC WFSS Lighting Installation	Northwest	624,179	624,233	-54	624,179	0	624,179	0	624,179	100.00%
SO SHPE Lighting Installation	South	596,302	596,302	-56,011	540,291	0	540,291	56,011	536,081	89.90%
SO SAUT Thermal Piping Installation	South	580,749	708,091	-127,342	580,749	0	580,749	0	580,749	100.00%

## Financial Summary Report

Description	Campus	BUDGET		COST COMMITMENTS				EXPENDITURES		
		A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
		Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
WFSO Fire Training LP Gas Line Replacement	Northwest	500,919	532,231	-31,312	500,919	0	500,919	0	500,919	100.00%
Pool Chemical Rooms	Districtwide	392,420	412,390	-19,970	392,420	0	392,420	0	392,420	100.00%
WFSC and WFSS DDC Controls Upgrade	Northwest	376,157	455,252	-79,095	376,157	0	376,157	0	376,157	100.00%
WFSC Fire Training Water Controls Upgrades	Northwest	357,794	373,548	-15,754	357,794	0	357,794	0	357,794	100.00%
NFAB Sprinkler Installation	Northeast	352,983	385,582	-32,599	352,983	0	352,983	0	352,983	100.00%
NE NBSA Air Handler Replacement	Northeast	344,678	346,952	-2,275	344,678	0	344,678	0	344,678	100.00%
SO SBUS Lighting Installation	South	342,851	342,357	-2,995	339,362	0	339,362	3,489	322,065	93.94%
Science Labs Gas Shutoff Controls	Districtwide	327,013	355,829	-28,816	327,013	0	327,013	0	327,013	100.00%
SO VB Drain/Ponding Repair	South	267,840	290,807	-22,967	267,840	0	267,840	0	267,840	100.00%
SETC Envelope Repairs Phase 2	South	262,256	282,698	-20,442	262,256	0	262,256	0	262,256	100.00%
Existing Air Compressor Systems Upgrade	South	256,003	282,034	-26,031	256,003	0	256,003	0	256,003	100.00%
SO SMTH Lighting Installation	South	214,092	214,092	-20,194	193,898	0	193,898	20,194	191,560	89.48%
Theater Audio and Lighting Repairs	Districtwide	164,697	174,684	-9,987	164,697	0	164,697	0	164,697	100.00%
Sanitary Sewer and Storm Drain Evaluation	Northeast	119,788	119,819	-31	119,788	0	119,788	0	119,788	100.00%
TR VB Lighting Installation	Trinity River	116,075	149,326	-33,251	116,075	0	116,075	0	116,075	100.00%
SCLC Sanitary Sewer and Drainage	South	115,839	124,682	-8,843	115,839	0	115,839	0	115,839	100.00%
SSCI Repairs AHU-8 and LEF-4	South	113,079	113,079	0	113,079	0	113,079	0	113,079	100.00%
Roof Drain, Water Infiltration and Grading Improvement Assessment	South	99,892	99,928	-35	99,892	0	99,892	0	99,892	100.00%
NFAB to NHPE Sewer Line Replacement	Northeast	80,159	83,972	-3,813	80,159	0	80,159	0	80,159	100.00%
SETC 1410 LG Training Center Lab Upgrade	South	75,460	82,700	-7,240	75,460	0	75,460	0	75,460	100.00%
DT NFAB Lighting Installation	Districtwide	70,634	70,634	0	70,634	0	70,634	0	37,135	52.57%
EBSA HVAC Upgrades	Southeast	67,348	71,921	-4,573	67,348	0	67,348	0	67,348	100.00%
NE and ODMC Exterior lighting Modifications	Northeast	60,073	62,410	-2,337	60,073	0	60,073	0	60,073	100.00%
4160 Utility Transformer Demo	Northeast	55,730	55,730	0	55,730	0	55,730	0	55,730	100.00%
TRPG and Data Center Nitrogen Generator Installation	Trinity River	52,365	52,365	0	52,365	0	52,365	0	52,365	100.00%
Baselines M and V for CC Campuses	Districtwide	46,648	49,200	-2,552	46,648	0	46,648	0	46,648	100.00%
NHSC Service Combination Upgrade	Northeast	43,524	44,148	-624	43,524	0	43,524	0	43,524	100.00%
SETC - 2009 HVAC Training Center Lab Upgrade	South	43,322	46,676	-3,354	43,322	0	43,322	0	43,322	100.00%
Chilled and Heating Water Loop Differential Pressure Study	Northwest	38,280	38,280	0	38,280	0	38,280	0	38,280	100.00%
EOC Fire Alarm Network Panel Removal	Trinity River	36,187	36,187	0	36,187	0	36,187	0	36,187	100.00%




# Financial Summary Report

	Campus	BUDGET		COST COMMITMENTS				EXPENDITURES		
		A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
Description		Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
SSTU DHW Study/Assessment	South	30,705	30,705	0	30,705	0	30,705	0	30,705	100.00%
SHPE RTAC 1 & 2 Replacement	South	21,545	21,545	0	21,545	0	21,545	0	21,545	100.00%
Study of Riser Underground Piping	Southeast	19,785	19,785	0	19,785	0	19,785	0	19,785	100.00%
NCAB & NSCE Install (2) Waterproof Covers & Ladders on (2) Transformers	Northeast	16,869	18,556	-1,687	16,869	0	16,869	0	16,869	100.00%
ECHS HVAC Upgrade	Southeast	16,376	16,376	0	16,376	0	16,376	0	16,376	100.00%
NFAB Transformer Replacement	Northeast	11,565	11,565	0	11,565	0	11,565	0	11,565	100.00%
ESED Transformer Replacement	Southeast	6,674	6,674	0	6,674	0	6,674	0	6,674	100.00%
ESCT Sprinkler Pipe Inspection	Southeast	2,800	9,720	-6,920	2,800	0	2,800	0	2,800	100.00%
NE NFAB Air Handler Replacement	Northeast	0	70,634	-70,634	0	0	0	0	0	0.00%
NW VB UPS and Backup Generator Installation	Northwest	0	0	0	0	0	0	0	0	0.00%
<b>Total for MEP / Infrastructure :</b>		<b>202,000,000</b>	<b>47,267,167</b>	<b>-2,589,404</b>	<b>44,677,763</b>	<b>0</b>	<b>44,677,763</b>	<b>157,322,237</b>	<b>36,474,208</b>	<b>0.00%</b>
<b>Total for Fund 90 :</b>		<b>825,000,000</b>	<b>251,717,993</b>	<b>2,984,527</b>	<b>254,702,520</b>	<b>0</b>	<b>254,702,520</b>	<b>570,297,480</b>	<b>132,840,079</b>	<b>16.10%</b>
<b>Fund 40</b>										
<b>NW Campus</b>										
Northwest VB Campus Re-Development	Northwest	64,000,000	1,773,356	618,978	2,392,334	0	2,392,334	61,607,666	710,725	1.11%
<b>Total for NW Campus :</b>		<b>64,000,000</b>	<b>1,773,356</b>	<b>618,978</b>	<b>2,392,334</b>	<b>0</b>	<b>2,392,334</b>	<b>61,607,666</b>	<b>710,725</b>	<b>1.11%</b>
<b>SE Campus</b>										
Southeast Campus Expansion	Southeast	29,990,000	1,647,595	0	1,647,595	0	1,647,595	28,342,405	0	0.00%
<b>Total for SE Campus :</b>		<b>29,990,000</b>	<b>1,647,595</b>	<b>0</b>	<b>1,647,595</b>	<b>0</b>	<b>1,647,595</b>	<b>28,342,405</b>	<b>0</b>	<b>0.00%</b>
<b>Total for Fund 40 :</b>		<b>93,990,000</b>	<b>3,420,951</b>	<b>618,978</b>	<b>4,039,929</b>	<b>0</b>	<b>4,039,929</b>	<b>89,950,071</b>	<b>710,725</b>	<b>0.76%</b>
<b>Fund 10</b>										
<b>SE Campus</b>										
Southeast Campus Expansion	Southeast	10,000	8,477	-2,717	5,760	0	5,760	4,240	5,760	57.60%
<b>Total for SE Campus :</b>		<b>10,000</b>	<b>8,477</b>	<b>-2,717</b>	<b>5,760</b>	<b>0</b>	<b>5,760</b>	<b>4,240</b>	<b>5,760</b>	<b>57.60%</b>
<b>Total for Fund 10 :</b>		<b>10,000</b>	<b>8,477</b>	<b>-2,717</b>	<b>5,760</b>	<b>0</b>	<b>5,760</b>	<b>4,240</b>	<b>5,760</b>	<b>57.60%</b>
<b>Grand Totals:</b>		<b>919,000,000</b>	<b>255,147,420</b>	<b>3,600,788</b>	<b>258,748,208</b>	<b>0</b>	<b>258,748,208</b>	<b>660,251,792</b>	<b>133,556,564</b>	<b>14.53%</b>


# Financial Summary Report

Report Date: 3/28/2022

Bond Budget by Fund

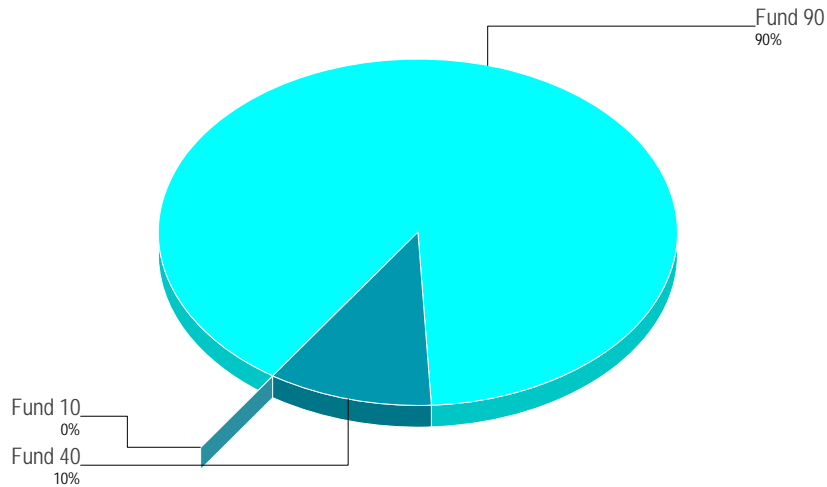

Budget Distribution by Fund & Campus

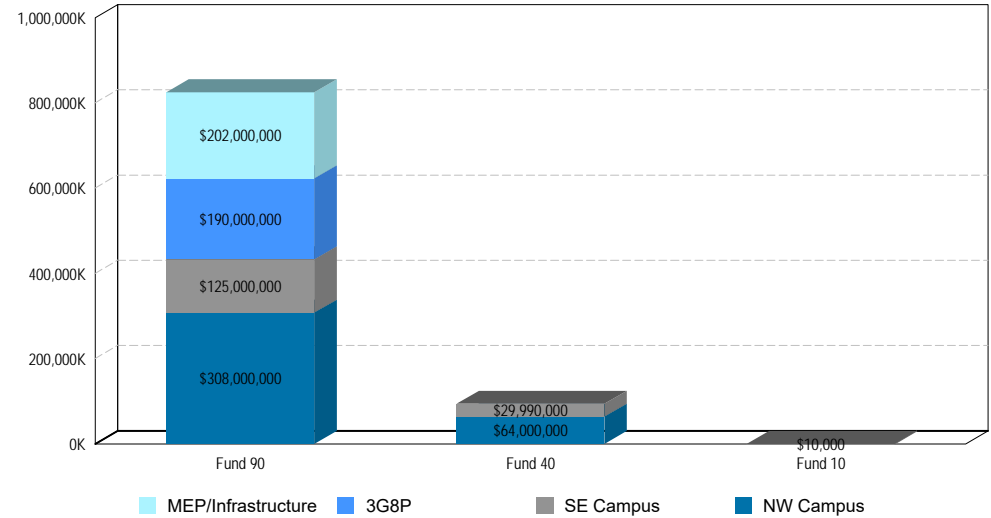

Description	BUDGET		COST COMMITMENTS				EXPENDITURES		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
<b>Fund 90</b>									
NW Campus :	308,000,000	161,444,788	-657,704	160,787,084	0	160,787,084	147,212,916	70,492,998	22.89%
SE Campus :	125,000,000	15,790,149	6,644,265	22,434,414	0	22,434,414	102,565,586	6,295,878	5.04%
3G8P :	190,000,000	27,215,888	-412,630	26,803,259	0	26,803,259	163,196,741	19,576,995	10.30%
MEP / Infrastructure :	202,000,000	47,267,167	-2,589,404	44,677,763	0	44,677,763	157,322,237	36,474,208	18.06%
<b>Total for Fund 90 :</b>	<b>825,000,000</b>	<b>251,717,993</b>	<b>2,984,527</b>	<b>254,702,520</b>	<b>0</b>	<b>254,702,520</b>	<b>570,297,480</b>	<b>132,840,079</b>	<b>16.10%</b>
<b>Fund 40</b>									
NW Campus :	64,000,000	1,773,356	618,978	2,392,334	0	2,392,334	61,607,666	710,725	1.11%
SE Campus :	29,990,000	1,647,595	0	1,647,595	0	1,647,595	28,342,405	0	0.00%
<b>Total for Fund 40 :</b>	<b>93,990,000</b>	<b>3,420,951</b>	<b>618,978</b>	<b>4,039,929</b>	<b>0</b>	<b>4,039,929</b>	<b>89,950,071</b>	<b>710,725</b>	<b>0.76%</b>
<b>Fund 10</b>									
SE Campus :	10,000	8,477	-2,717	5,760	0	5,760	4,240	5,760	57.60%
<b>Total for Fund 10 :</b>	<b>10,000</b>	<b>8,477</b>	<b>-2,717</b>	<b>5,760</b>	<b>0</b>	<b>5,760</b>	<b>4,240</b>	<b>5,760</b>	<b>57.60%</b>
<b>Grand Totals:</b>	<b>919,000,000</b>	<b>255,147,420</b>	<b>3,600,788</b>	<b>258,748,208</b>	<b>0</b>	<b>258,748,208</b>	<b>660,251,792</b>	<b>133,556,564</b>	<b>14.53%</b>

NW Campus

## PROJECT DESCRIPTION/TEAM

Project Name: NW VB Campus Re-Development

Address: 4801 Marine Creek Parkway  
Fort Worth  
TX

Project Type: Capital Improvement

Project Phase: Construction

Architect: Huckabee + Gensler

CMAR: Skanska USA Building Inc.

## PROJECT SCOPE

Re-Development of the NW Campus including demolition, renovations, infrastructure, and new construction

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	21-Sep-2018	21-Sep-2018	0.00	↑
Design Start	07-Oct-2019			↑
Design Finish	16-Oct-2019			↑
Pre-construction Meeting	12-Dec-2019			↑
Construction Start	13-Dec-2019			↑
Substantial Completion Date	08-Dec-2025			↑
Construction Finish (Final Completion)	30-Dec-2025			↑
Close Out Start	31-Dec-2025			↑
Close Out Finish	12-Feb-2026			↑
Warranty Walk Due	27-Feb-2026			↑


↑ Overtime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Mar 23, 2022: Construction progress in March for Buildings 1 and 2 by the Skanska USA Buildings Inc (Skanska) construction team continued to show positive major achievements. As Skanska targets the next major milestone to "dry-in" the new buildings, installation of roofing and water-proof siding has started. Skanska is also continuing with interior metal wall framing, mechanical and plumbing system installations, and rough-in of electrical systems. All slab on grade and elevated concrete slab work has been completed. Door frames are being installed and window frames and glass are tracking to begin in early April. The construction schedule continues to track on time, as expected, with rigorous review to mitigate minor delays resulting from weather impacts and taking advantage of opportunities to make schedule gains through well thought out plans and contingencies.

## BUDGET/COST STATUS

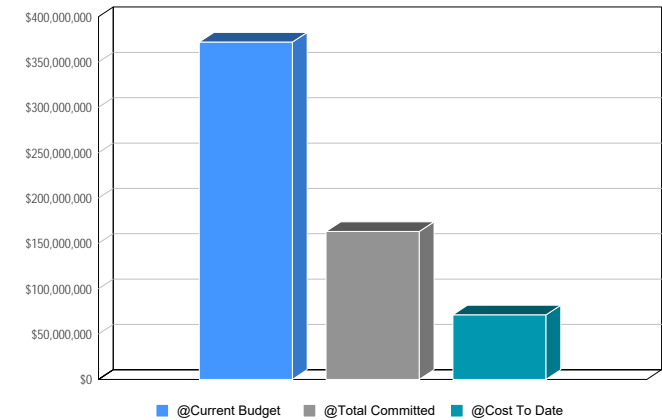

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	40,301,484	37,690,632	-285	37,690,347	0	37,690,347	2,611,137	23,246,683	57.68%
02. Hard Cost	291,631,116	125,399,969	0	125,399,969	0	125,399,969	166,231,147	47,867,938	16.41%
03. FF&E	25,036,104	127,543	-38,441	89,102	0	89,102	24,947,002	89,102	0.36%
04. Project Contingency	15,031,296	0	0	0	0	0	15,031,296	0	0.00%
<b>Total:</b>	<b>372,000,000</b>	<b>163,218,144</b>	<b>-38,726</b>	<b>163,179,418</b>	<b>0</b>	<b>163,179,418</b>	<b>208,820,582</b>	<b>71,203,723</b>	<b>19.14%</b>

## SE Campus

### PROJECT DESCRIPTION/TEAM

Project Name: SE VB Campus Expansion

Address: 2100 Southeast Pkwy  
Arlington  
TX

Project Type: Capital Improvement

Project Phase: Bidding

Architect: Perkins & Will

CMAR: Cable's Plumbing

### PROJECT SCOPE

The project consists of the renovation and expansion of the Tarrant County College District's Southeast Campus. The renovation scope will include selective structural renovation, major renovation, and finish level renovation to address campus needs and district-wide initiatives, and to fit contextually within the overall design concept to create a new campus identity. The renovation will also include selective façade and building envelope updates. The new construction scope will consist of two buildings. The North Building will serve as the front door to the campus for visitors and prospective students. It will include a Welcome Center, Financial Aid, Business Services, Admission, Testing, Onboarding, Advising, and other related programs. The South Building will serve as a gateway from the south, primarily for current students. It will include General Classrooms, Labs, Faculty Workspace, and Culinary. Exterior spaces including two main courtyards will also serve as an integral part of the concept design. The site scope is also inclusive of the redevelopment of the main access drive and the addition of a paved parking lot on the east side of campus.

### PROJECT PHOTO



### SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	06-May-2019	06-May-2019	0.00	↑
Design Start	24-May-2019	24-May-2019	0.00	↑
Anticipated - Commitment - Commissioning	12-Oct-2021			↑
Anticipated - Commitment - T&B	01-Dec-2021			↑
Design Finish	20-Jan-2022			↑
Pre-construction Meeting	08-Mar-2022			↑
Construction Start	09-Mar-2022			↑
Substantial Completion Date	30-Nov-2023			↑
Construction Finish (Final Completion)	01-Dec-2023			↑
Close Out Start	04-Dec-2023			↑
Close Out Finish	16-Jan-2024			↑
Warranty Walk Due	20-Sep-2024			↑


↑ Ontime/Early      ↓ Delayed/ Late

### PROGRESS SUMMARY

Feb 22, 2022: March 2022 Status Update

1. BPH Mobilized on Southeast Campus
2. BPH began Utility locates and relocation
3. BPH started bidding process for GMP-1, New Construction of Building 1 and Building 7
4. BPH procured WA-1 Utility Relocate City of Arlington Building Permit
5. Site Logistics plan has been implemented around Southeast Campus construction zones

### BUDGET/COST STATUS

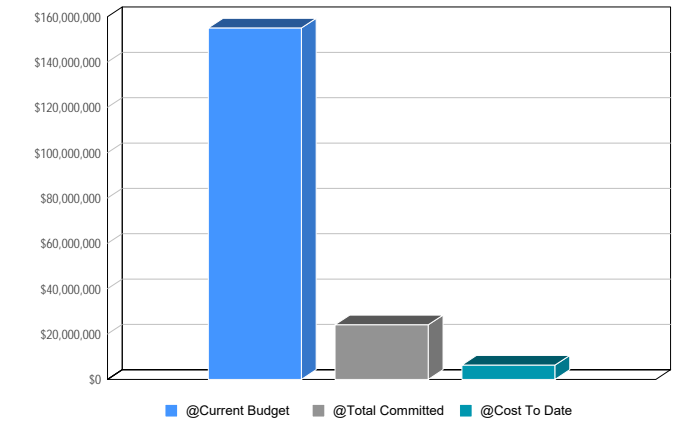

### FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	18,007,187	9,776,261	6,641,548	16,417,810	0	16,417,810	1,589,377	6,137,928	34.09%
02. Hard Cost	116,635,572	7,669,959	0	7,669,959	0	7,669,959	108,965,613	163,710	0.14%
03. FF&E	12,000,000	0	0	0	0	0	12,000,000	0	0.00%
04. Project Contingency	8,357,241	0	0	0	0	0	8,357,241	0	0.00%
<b>Total:</b>	<b>155,000,000</b>	<b>17,446,220</b>	<b>6,641,548</b>	<b>24,087,769</b>	<b>0</b>	<b>24,087,769</b>	<b>130,912,231</b>	<b>6,301,638</b>	<b>4.07%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: DT VB Generator Installation

Address: 828 W. Harwood Road

Hurst

TX

Project Type: MEP

Project Phase: Planning

Architect:

CMAR:

## PROJECT SCOPE

NE Campus backup power for lighting, IT, and critical infrastructure life safety systems.

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	29-May-2019	29-May-2019	0.00	↑
Design Start	16-Jun-2021			↑
Close Out Finish	31-Aug-2021			↑
Design Finish	04-Nov-2021			↑
Pre-construction Meeting	30-Dec-2021			↑
Construction Start	31-Dec-2021			↑
Substantial Completion Date	08-Mar-2022			↑
Construction Finish (Final Completion)	24-Mar-2022			↑
Close Out Start	25-Mar-2022			↑
Warranty Walk Due	28-Dec-2022			↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Mar 23, 2022: Working to verify project budget and scope in preparation for Work Induction Board Phase II Presentation.

## BUDGET/COST STATUS

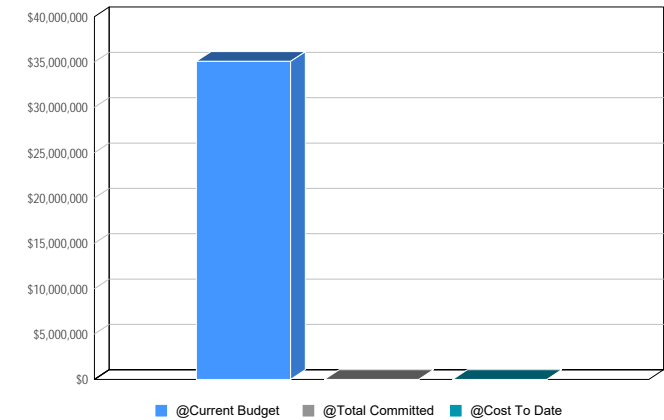

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	2,890,000	0	0	0	0	0	2,890,000	0	0.00%
02. Hard Cost	30,476,000	0	0	0	0	0	30,476,000	0	0.00%
03. FF&E	0	0	0	0	0	0	0	0	0.00%
04. Project Contingency	1,725,000	0	0	0	0	0	1,725,000	0	0.00%
<b>Total:</b>	<b>35,091,000</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>0</b>	<b>35,091,000</b>	<b>0</b>	<b>0.00%</b>

3G8P

**PROJECT DESCRIPTION/TEAM**

Project Name: DT NTAB and SCAB/D Classrooms Renovations

Address: 5450 N. Riverside Drive  
Fort Worth  
TX

Project Type: Renovation

Project Phase: Design

Architect: Bennett Benner Partners, Inc.

CMAR:

**PROJECT SCOPE**

This project seeks to bring poor and fair as well as previously upgraded basic condition classrooms in line with the IILE Principle as part of the 3G8P efforts for both North East Campus NTAB building and the South Campus SACB/SACD buildings. Refinish of the existing hallways and common spaces as well as necessary ADA updates to restroom facilities are also planned as part of the project scope. A Fire Sprinkler system will be added to the entire NTAB facility.

**PROJECT PHOTO**



**SCHEDULE**

Description	Target Finish	Current Finish	Variance	
Notification of Project Commencement	08-Nov-2021	08-Nov-2021	0.00	↑
Finish Review - Comply with TCC Stand	29-Nov-2021			↑
Interior Design Review - Materials/Furnitu	29-Nov-2021			↑
Vacate Date of Existing Spaces	10-Jan-2022			↑
Swing Space Activation Notification	10-Jan-2022			↑
Discussion of OFCI Items	10-Jan-2022			↑
Interior Design Review - Materials/Furnitu	10-Jan-2022			↑
Finish Review - Comply with TCC Stand	21-Feb-2022			↑

↑ Ontime/Early


↓ Delayed/ Late

**PROGRESS SUMMARY**

Mar 23, 2022: Design team resubmitted the design development package, it's been reviewed and comments were given to the architect.

50% Construction drawings set has been sent to the Bond team and it is in review session for comments.

**BUDGET/COST STATUS**

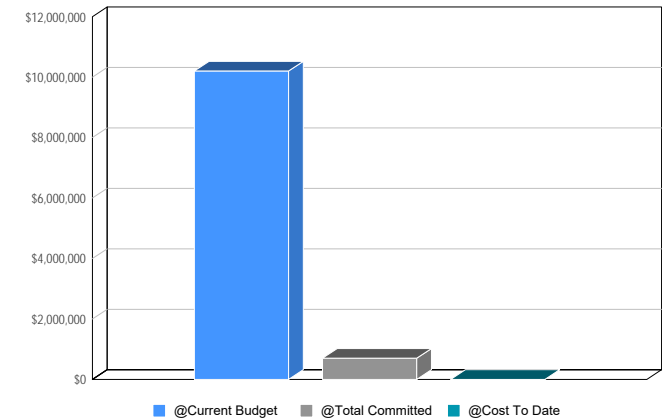

**FINANCIAL STATUS**

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	898,250	699,250	0	699,250	0	699,250	199,000	0	0.00%
02. Hard Cost	4,901,722	0	0	0	0	0	4,901,722	0	0.00%
03. FF&E	3,437,000	0	0	0	0	0	3,437,000	0	0.00%
04. Project Contingency	965,156	0	0	0	0	0	965,156	0	0.00%
<b>Total:</b>	<b>10,202,128</b>	<b>699,250</b>	<b>0</b>	<b>699,250</b>	<b>0</b>	<b>699,250</b>	<b>9,502,878</b>	<b>0</b>	<b>0.00%</b>

Districtwide

3G8P

**PROJECT DESCRIPTION/TEAM**

Project Name: DT VB IILE Classroom Renovation

Address: 5450 N. Riverside Drive  
Fort Worth  
TX

Project Type: Capital Improvement

Project Phase: Close out

Architect: Hahnfeld Hoffer Stanford

CMAR:

**PROJECT SCOPE**

Upgrade select classrooms in the District to a Formal Learning and a Formal Learning Tech Plus level according to IILE guidelines.

**PROJECT PHOTO**



**SCHEDULE**

Description	Target Finish	Current Finish	Variance	
Project Created Date	09-Sep-2020	09-Sep-2020	0.00	↑
Design Start	22-Oct-2020	22-Oct-2020	0.00	↑
Design Finish	01-Apr-2021	01-Apr-2021	0.00	↑
Pre-construction Meeting	07-Jun-2021	07-Jun-2021	0.00	↑
Construction Start	08-Jun-2021	08-Jun-2021	0.00	↑
Substantial Completion Date	07-Sep-2021	07-Sep-2021	0.00	↑
Construction Finish (Final Completion)	17-Dec-2021			↑
Close Out Start	20-Dec-2021			↑
Close Out Finish	07-Jan-2022			↑


↑ Overtime/Early

↓ Delayed/ Late

**PROGRESS SUMMARY**

Mar 23, 2022: The classrooms are complete and closeouts are in progress.

**BUDGET/COST STATUS**

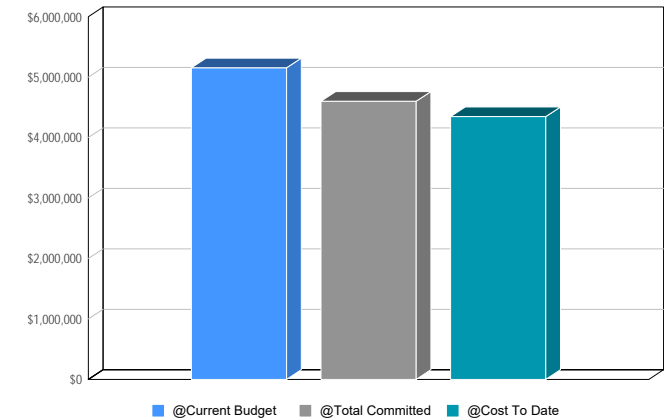

**FINANCIAL STATUS**

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	249,020	249,020	-2,051	246,969	0	246,969	2,051	228,405	91.72%
02. Hard Cost	3,337,493	3,491,094	0	3,491,094	0	3,491,094	-153,601	3,292,937	98.66%
03. FF&E	831,757	862,564	0	862,564	0	862,564	-30,807	826,923	99.42%
04. Project Contingency	735,433	0	0	0	0	0	735,433	0	0.00%
<b>Total:</b>	<b>5,153,702</b>	<b>4,602,678</b>	<b>-2,051</b>	<b>4,600,628</b>	<b>0</b>	<b>4,600,628</b>	<b>553,075</b>	<b>4,348,265</b>	<b>84.37%</b>

Districtwide

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: NW VB Power Installation

Address: 4801 Marine Creek Parkway

Fort Worth

TX

Project Type: MEP

Project Phase: Construction

Architect: Yaggi Engineering, Inc.

CMAR: Facility Solutions Group

## PROJECT SCOPE

This Project scope includes the replacement of all electrical utility infrastructure that serves the entire Northwest Campus. This includes all new pipe, wire, transformers, and switches for the Medium Voltage System that serves NW buildings power.

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	16-Dec-2016	16-Dec-2016	0.00	↑
Design Start	09-Jan-2017	09-Jan-2017	0.00	↑
Design Finish	10-Jan-2019	10-Jan-2019	0.00	↑
Pre-construction Meeting	29-Mar-2019	29-Mar-2019	0.00	↑
Construction Start	01-Apr-2019	01-Apr-2019	0.00	↑
Substantial Completion Date	04-Jun-2020	04-Jun-2020	0.00	↑
Construction Finish (Final Completion)	25-Dec-2020	25-Dec-2020	0.00	↑
Close Out Start	28-Dec-2020	28-Dec-2020	0.00	↑
Close Out Finish	22-Jul-2021			↑


↑ Overtime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 22, 2022: Project complete working on final billing

## BUDGET/COST STATUS

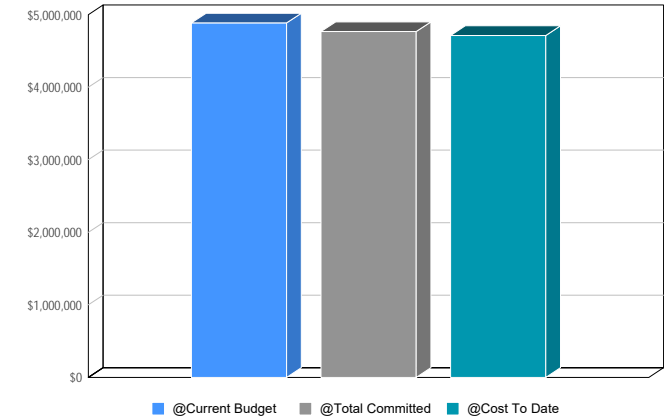

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	374,204	359,204	-56,533	302,671	0	302,671	71,533	248,807	66.49%
02. Hard Cost	3,523,304	3,523,304	-47,370	3,475,934	0	3,475,934	47,370	3,475,934	98.66%
03. FF&E	988,859	994,863	-6,004	988,859	0	988,859	0	988,859	100.00%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>4,886,367</b>	<b>4,877,371</b>	<b>-109,907</b>	<b>4,767,464</b>	<b>0</b>	<b>4,767,464</b>	<b>118,903</b>	<b>4,713,600</b>	<b>96.46%</b>



3G8P

**PROJECT DESCRIPTION/TEAM**

Project Name: OWTL Corporate Services Renovation

Address: 2301 Horizon Drive  
Fort Worth  
TX

Project Type: Renovation

Project Phase: Completed

Architect: Lockwood, Andrews & Newnam Inc.

CMAR: Imperial Construction, Inc.

**PROJECT SCOPE**

Engage a design professional to program OWTL related to the 3rd Floor conversion to Corporate Services and the need to relocate college services from this floor.

**PROJECT PHOTO**



**SCHEDULE**

Description	Target Finish	Current Finish	Variance	
Project Created Date	13-Feb-2020	13-Feb-2020	0.00	↑
Design Start	17-Apr-2020	17-Apr-2020	0.00	↑
Design Finish	24-Jul-2020	24-Jul-2020	0.00	↑
Pre-construction Meeting	23-Sep-2020	23-Sep-2020	0.00	↑
Construction Start	25-Sep-2020	25-Sep-2020	0.00	↑
Substantial Completion Date	18-May-2021	16-Feb-2021	91.00	↑
Construction Finish (Final Completion)	26-Jul-2021	26-Jul-2021	0.00	↑
Close Out Start	27-Jul-2021	27-Jul-2021	0.00	↑
Close Out Finish	14-Sep-2021	14-Sep-2021	0.00	↑


↑ Overtime/Early

↓ Delayed/ Late

**PROGRESS SUMMARY**

Mar 23, 2022: The project is complete. A final Budget Change Request to zero out the project budget has been submitted, once approved the project will be closed.

**BUDGET/COST STATUS**

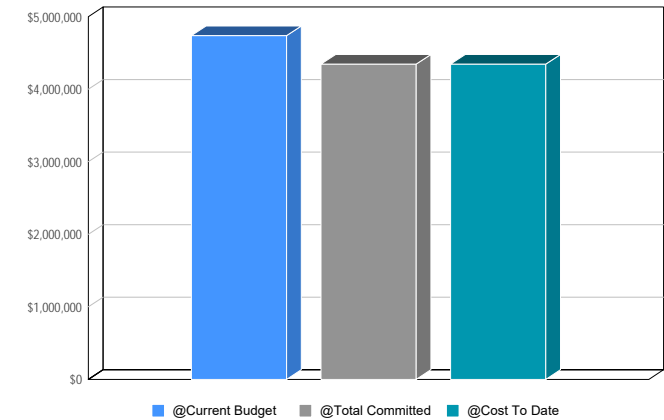

**FINANCIAL STATUS**

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	461,320	599,949	-2,352	597,597	0	597,597	-136,277	597,597	129.54%
02. Hard Cost	2,797,524	2,498,373	-129,433	2,368,940	0	2,368,940	428,584	2,368,940	84.68%
03. FF&E	1,280,276	1,492,038	-112,055	1,379,983	0	1,379,983	-99,707	1,379,983	107.79%
04. Project Contingency	199,350	0	0	0	0	0	199,350	0	0.00%
<b>Total:</b>	<b>4,738,470</b>	<b>4,590,360</b>	<b>-243,841</b>	<b>4,346,520</b>	<b>0</b>	<b>4,346,520</b>	<b>391,950</b>	<b>4,346,520</b>	<b>91.73%</b>

## PROJECT DESCRIPTION/TEAM

Project Name: OWTL Welding Lab Expansion

Address: 2301 Horizon Drive

Fort Worth

TX

Project Type: Renovation

Project Phase: Close out

Architect: JQ Engineering, LLP

CMAR: Gomez Floor Covering

## PROJECT SCOPE

This project will entail the retrofit of the existing Oxy-acetylene welding lab into a Tig welding lab, scopes of work will include upgraded electrical and air filtration systems, installation of a demising partition and thirteen new welding machines.

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	25-Apr-2018	25-Apr-2018	0.00	↑
Design Start	26-Sep-2018	26-Sep-2018	0.00	↑
Design Finish	23-Jun-2020	23-Jun-2020	0.00	↑
Pre-construction Meeting	14-Sep-2020	14-Sep-2020	0.00	↑
Construction Start	15-Sep-2020	15-Sep-2020	0.00	↑
Substantial Completion Date	10-Sep-2021			↑
Construction Finish (Final Completion)	04-Oct-2021			↑
Close Out Start	05-Oct-2021			↑
Close Out Finish	17-Nov-2021			↑
Warranty Walk Due	04-Jul-2022			↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 23, 2022: Construction is 100% complete. The project is in the close out phase. Final invoicing and the close out manuals have been requested from the general contractor.

## BUDGET/COST STATUS

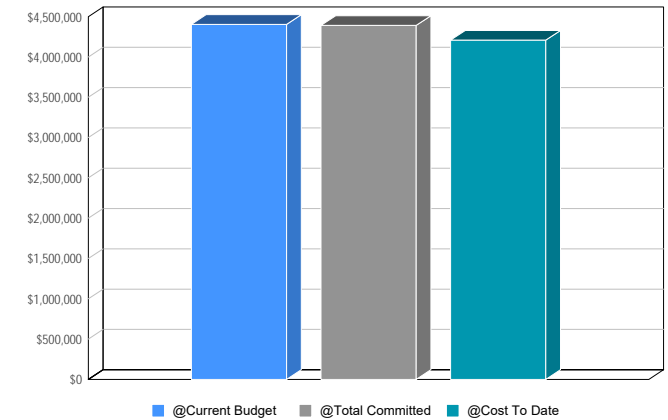

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	329,170	333,607	0	333,607	0	333,607	-4,437	330,220	100.32%
02. Hard Cost	3,564,061	3,191,624	-3,000	3,188,624	0	3,188,624	375,437	3,013,160	84.54%
03. FF&E	511,610	870,396	0	870,396	0	870,396	-358,786	865,315	169.14%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>4,404,841</b>	<b>4,395,626</b>	<b>-3,000</b>	<b>4,392,626</b>	<b>0</b>	<b>4,392,626</b>	<b>12,214</b>	<b>4,208,695</b>	<b>95.55%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: NW WBSP Chiller/Cooling Towers Replacement

Address: 4801 Marine Creek Parkway

Fort Worth

TX

Project Type: MEP

Project Phase: Construction

Architect: Summit Consultants

CMAR: Infinity Contractors International LTD

## PROJECT SCOPE

NW Campus Chiller and Cooling Tower Upgrade design.

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	09-Jul-2019	09-Jul-2019	0.00	↑
Design Start	03-Sep-2019	02-Sep-2019	1.00	↑
Design Finish	24-Mar-2020	02-Mar-2020	22.00	↑
Pre-construction Meeting	27-Oct-2020	29-Oct-2020	-2.00	↓
Construction Start	08-Dec-2020	08-Dec-2020	0.00	↑
Substantial Completion Date	14-Oct-2021	14-Oct-2021	0.00	↑
Construction Finish (Final Completion)	05-Nov-2021	05-Nov-2021	0.00	↑
Close Out Start	08-Nov-2021	08-Nov-2021	0.00	↑
Close Out Finish	26-Apr-2022			↑
Warranty Walk Due	05-Aug-2022			↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 22, 2022: CX is progressing. Working on close-out

## BUDGET/COST STATUS

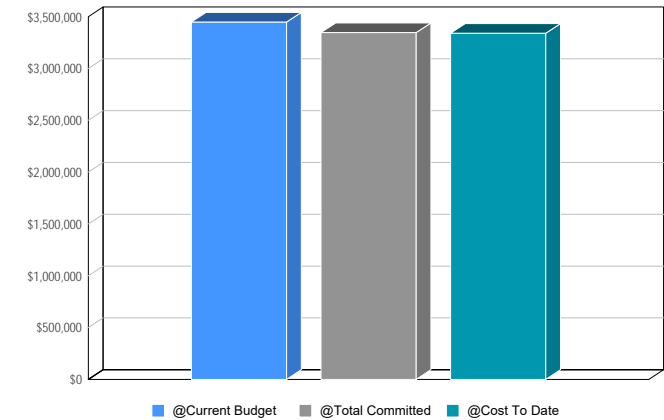

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	300,605	300,605	-5,939	294,666	0	294,666	5,939	289,229	96.22%
02. Hard Cost	1,715,788	1,557,338	-26,468	1,530,870	0	1,530,870	184,918	1,530,870	89.22%
03. FF&E	1,432,000	1,520,483	0	1,520,483	0	1,520,483	-88,483	1,520,483	106.18%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>3,448,393</b>	<b>3,378,426</b>	<b>-32,407</b>	<b>3,346,019</b>	<b>0</b>	<b>3,346,019</b>	<b>102,374</b>	<b>3,340,583</b>	<b>96.87%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: SE EBSP Cooling Tower Replacement

Address: 2100 Southeast Pkwy  
Arlington  
TX

Project Type: MEP

Project Phase: Close out

Architect: Shah Smith & Associates

CMAR: Infinity Contractors International LTD

## PROJECT SCOPE

South Campus study to determine the location for a new Cooling Tower, including the Design, Purchase, and Installation of the new Cooling Tower.

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	22-Mar-2019	22-Mar-2019	0.00	↑
Design Start	22-May-2019	22-May-2019	0.00	↑
Design Finish	16-Dec-2019	02-Jan-2020	-17.00	↓
Pre-construction Meeting	27-Feb-2020	27-Feb-2020	0.00	↑
Construction Start	27-Feb-2020	27-Feb-2020	0.00	↑
Substantial Completion Date	20-Nov-2020	20-Nov-2020	0.00	↑
Construction Finish (Final Completion)	22-Dec-2020	22-Dec-2020	0.00	↑
Close Out Start	24-Dec-2020	24-Dec-2020	0.00	↑
Close Out Finish	14-Mar-2022	14-Mar-2022	0.00	↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 22, 2022: Working on close-out

## BUDGET/COST STATUS

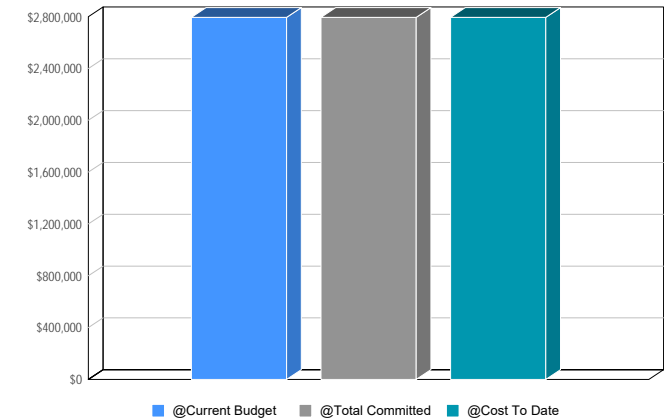

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	275,377	306,192	-30,814	275,377	0	275,377	0	275,377	100.00%
02. Hard Cost	2,023,167	2,099,619	-76,452	2,023,167	0	2,023,167	0	2,023,167	100.00%
03. FF&E	496,582	496,582	0	496,582	0	496,582	0	496,582	100.00%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>2,795,126</b>	<b>2,902,392</b>	<b>-107,266</b>	<b>2,795,126</b>	<b>0</b>	<b>2,795,126</b>	<b>0</b>	<b>2,795,126</b>	<b>100.00%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: SE EBSP Chiller Replacement

Address: 2100 Southeast Pkwy  
Arlington  
TX

Project Type: Capital Improvement

Project Phase: Construction

Architect: Summit Consultants

CMAR: Texas Air Systems & Johnson Controls

## PROJECT SCOPE

Replacement of two chillers

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Start	14-Oct-2020	14-Oct-2020	0.00	↑
Design	26-Apr-2021	26-Apr-2021	0.00	↑
Finish Review - Comply with TCC Stand	29-Nov-2021			↑
Vacate Date of Existing Spaces	10-Jan-2022			↑
Site Logistics Review as it relates to Proje	10-Jan-2022			↑
Security, Access Control & Keying Meetin	10-Jan-2022			↑
Interior Design Review - Materials/Furnitu	10-Jan-2022			↑
Finish Review - Comply with TCC Stand	10-Jan-2022			↑
Interior Design - Materials/Furniture/Finis	21-Feb-2022			↑
Construction	25-Apr-2022			↑
Substantial Completion	26-Apr-2022			↑
Project Closeout	21-Jun-2022			↑


↑ Overtime/Early      ↓ Delayed/ Late

## PROGRESS SUMMARY

Mar 23, 2022: Contractor installed isolation valves on for the two new chillers. Start installation for the low voltage wiring for the new light fixtures.

Manufacture confirmed that we are still on track for chillers manufacturing is complete on 3/25 and shipping will follow. contractor submitted all materials included in the project for engineer of record review and approval.

## BUDGET/COST STATUS

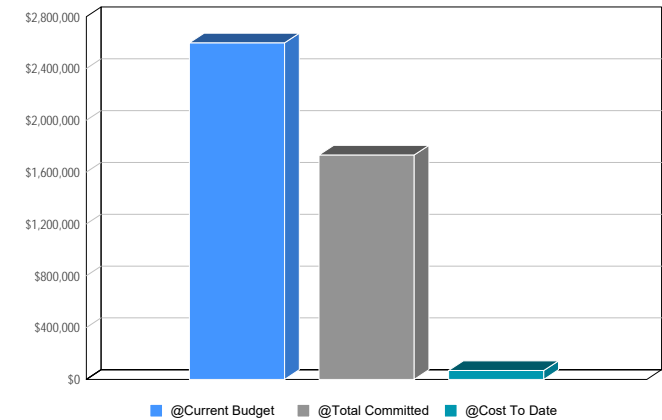

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	201,248	120,248	0	120,248	0	120,248	81,000	68,775	34.17%
02. Hard Cost	1,611,878	2,579,878	-968,000	1,611,878	0	1,611,878	0	0	0.00%
03. FF&E	0	0	0	0	0	0	0	0	0.00%
04. Project Contingency	785,180	0	0	0	0	0	785,180	0	0.00%
<b>Total:</b>	<b>2,598,305</b>	<b>2,700,126</b>	<b>-968,000</b>	<b>1,732,126</b>	<b>0</b>	<b>1,732,126</b>	<b>866,180</b>	<b>68,775</b>	<b>2.65%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: **SO VB UPS and Generator Installation**

Address: 5301 Campus Drive  
Fort Worth  
TX

Project Type: MEP

Project Phase: Construction

Architect: Yaggi Engineering, Inc.  
CMAR: Brandt Engineering

## PROJECT SCOPE

South Campus East Generator and Distribution Design for buildings SECH, SBSP, SBSA, SBSB, SELE, SHPE, STEC, SACR, SMTH

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	04-Dec-2015	04-Dec-2015	0.00	↑
Design Start	04-Dec-2015	04-Dec-2015	0.00	↑
Design Finish	05-Sep-2018	05-Sep-2018	0.00	↑
Pre-construction Meeting	24-Jan-2019	24-Jan-2019	0.00	↑
Construction Start	24-Jan-2019	24-Jan-2019	0.00	↑
Close Out Start	09-Jun-2021	26-Jul-2019	684.00	↑
Substantial Completion Date	30-Jun-2021	22-Feb-2022	-237.00	↓
Construction Finish (Final Completion)	30-Jun-2021	22-Feb-2022	-237.00	↓
Close Out Finish	20-Dec-2021			↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 22, 2022: In final billing for UPS portion project construction complete

## BUDGET/COST STATUS

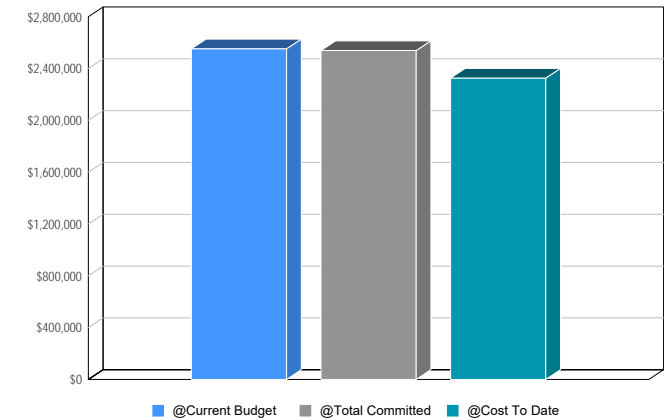

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	344,761	349,531	0	349,531	0	349,531	-4,770	349,531	101.38%
02. Hard Cost	1,551,387	1,571,005	-37,303	1,533,702	0	1,533,702	17,685	1,324,082	85.35%
03. FF&E	655,917	662,889	-6,972	655,917	0	655,917	0	652,832	99.53%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>2,552,065</b>	<b>2,583,424</b>	<b>-44,275</b>	<b>2,539,149</b>	<b>0</b>	<b>2,539,149</b>	<b>12,916</b>	<b>2,326,444</b>	<b>91.16%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: NE VB Sewer Rehabilitation

Address: 828 W. Harwood Road

Hurst

TX

Project Type: MEP

Project Phase: Construction

Architect: Carrillo Engineering, LLC

CMAR: Cable's Plumbing

## PROJECT SCOPE

This project is to replace all in ground sewer mains at Northeast Campus that are 50+ years old and have met their life cycle.

## PROJECT PHOTO



## SCHEDULE


Description	Target Finish	Current Finish	Variance
Vacate Date of Existing Spaces	10-Jan-2022		↑
Swing Space Activation Notification	10-Jan-2022		↑
Site Logistics Review as it relates to Proje	10-Jan-2022		↑
Security, Access Control & Keying Meetin	10-Jan-2022		↑
Interior Design Review - Materials/Furnitu	10-Jan-2022		↑
Finish Review - Comply with TCC Standar	10-Jan-2022		↑
Design	15-Apr-2022		↑
Enter Intended Board Meeting Approval D	21-Apr-2022		↑
Substantial Completion	23-Dec-2022		↑
Construction	03-Feb-2023		↑
Project Closeout	02-Feb-2023		↑

↑ Ontime/Early      ↓ Delayed/ Late

## PROGRESS SUMMARY

Mar 23, 2022: The draft board memo for approval of the construction contracts was submitted for preliminary review on 03/23/2022. The contract has been signed by contractor and is set for approval at the April 2022 Board meeting.

## BUDGET/COST STATUS

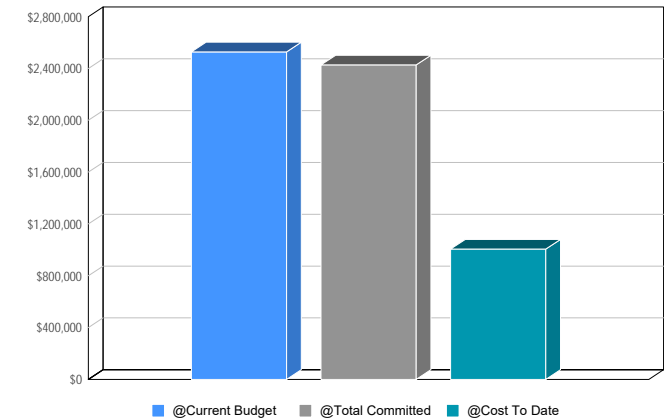

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	94,583	94,583	0	94,583	0	94,583	0	84,353	89.18%
02. Hard Cost	2,405,000	2,391,689	-58,274	2,333,415	0	2,333,415	71,585	921,287	38.31%
03. FF&E	0	0	0	0	0	0	0	0	0.00%
04. Project Contingency	28,917	0	0	0	0	0	28,917	0	0.00%
<b>Total:</b>	<b>2,528,500</b>	<b>2,486,273</b>	<b>-58,274</b>	<b>2,427,998</b>	<b>0</b>	<b>2,427,998</b>	<b>100,502</b>	<b>1,005,640</b>	<b>39.77%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: NE NBSP Boiler Replacement

Address: 828 W. Harwood Road

Hurst

TX

Project Type: MEP

Project Phase: Close out

Architect: Farnsworth Group, Inc.

CMAR: Texas Refrigeration, Inc.

## PROJECT SCOPE

NE Heating Water Boiler upgrade, Domestic Hot Water Boiler upgrade & Connect NHPE to hot water loop

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	19-Feb-2020	19-Feb-2020	0.00	↑
Design Start	16-Mar-2020	16-Mar-2020	0.00	↑
Design Finish	24-Apr-2020	24-Apr-2020	0.00	↑
Pre-construction Meeting	19-May-2020	19-May-2020	0.00	↑
Construction Start	20-May-2020	20-May-2020	0.00	↑
Substantial Completion Date	18-Nov-2020	18-Nov-2020	0.00	↑
Construction Finish (Final Completion)	18-Dec-2020	18-Dec-2020	0.00	↑
Close Out Start	21-Dec-2020	21-Dec-2020	0.00	↑
Close Out Finish	07-Dec-2021	07-Dec-2021	0.00	↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 22, 2022: Project complete

## BUDGET/COST STATUS

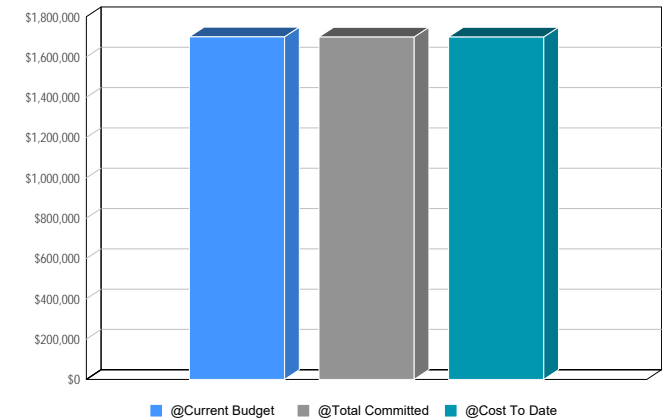

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	123,662	128,565	-5,368	123,197	0	123,197	465	123,197	99.62%
02. Hard Cost	1,249,921	1,288,331	-38,411	1,249,921	0	1,249,921	0	1,249,921	100.00%
03. FF&E	326,579	326,579	0	326,579	0	326,579	0	326,579	100.00%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>1,700,161</b>	<b>1,743,475</b>	<b>-43,779</b>	<b>1,699,696</b>	<b>0</b>	<b>1,699,696</b>	<b>465</b>	<b>1,699,696</b>	<b>99.97%</b>



MEP / Infrastructure

PROJECT DESCRIPTION/TEAM
Project Name: SE VB Generator Installation
Address: 2100 Southeast Pkwy Arlington TX
Project Type: MEP
Project Phase: Construction
Architect: Yaggi Engineering, Inc.
CMAR: Fort Worth Electric, L P


PROJECT SCOPE
SE Campus Emergency Generator to provide an alternate backup power source.



SCHEDULE			
Description	Target Finish	Current Finish	Variance
Project Created Date	29-May-2019	29-May-2019	0.00 ↑
Construction Start	17-Jun-2019	19-Aug-2019	-63.00 ↓
Design Start	16-Jul-2019	16-Jul-2019	0.00 ↑
Close Out Start	30-Sep-2019	30-Sep-2019	0.00 ↑
Design Finish	25-Feb-2020	25-Feb-2020	0.00 ↑
Pre-construction Meeting	27-Mar-2020		↑
Substantial Completion Date	23-Sep-2021		↑
Construction Finish (Final Completion)	23-Sep-2021		↑
Close Out Finish	10-Jan-2022		↑
Warranty Walk Due	15-Jul-2022		↑

↑ Overtime/Early      ↓ Delayed/ Late

PROGRESS SUMMARY
Feb 22, 2022: Project complete, Project Manager working on closeout and processing of final billing.

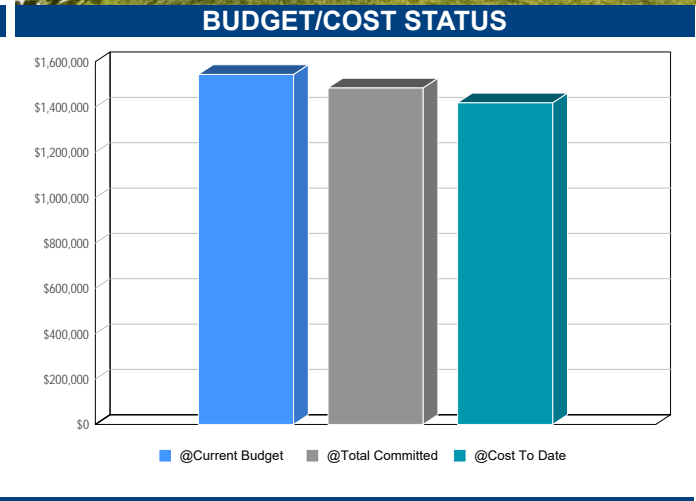

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	173,694	176,745	28	176,773	0	176,773	-3,079	171,223	98.58%
02. Hard Cost	1,222,560	1,227,260	-67,862	1,159,398	0	1,159,398	63,162	1,099,306	89.92%
03. FF&E	147,677	147,677	610	148,287	0	148,287	-610	148,287	100.41%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>1,543,930</b>	<b>1,551,682</b>	<b>-67,224</b>	<b>1,484,457</b>	<b>0</b>	<b>1,484,457</b>	<b>59,473</b>	<b>1,418,816</b>	<b>91.90%</b>

MEP / Infrastructure

## PROJECT DESCRIPTION/TEAM

Project Name: SE VB UPS and Generator Installation

Address: 2100 Southeast Pkwy  
Arlington  
TX

Project Type: MEP

Project Phase: Construction

Architect: Yaggi Engineering, Inc.  
CMAR: Fort Worth Electric, L P

## PROJECT SCOPE

SE Campus Emergency Power/Standby System Upgrade Design

## PROJECT PHOTO



## SCHEDULE

Description	Target Finish	Current Finish	Variance	
Project Created Date	27-Jan-2017	27-Jan-2017	0.00	↑
Design Start	15-Feb-2017	15-Feb-2017	0.00	↑
Design Finish	11-Sep-2018	11-Sep-2018	0.00	↑
Pre-construction Meeting	31-Jan-2019	31-Jan-2019	0.00	↑
Construction Start	01-Feb-2019	01-Feb-2019	0.00	↑
Substantial Completion Date	16-Jul-2021	16-Jul-2021	0.00	↑
Construction Finish (Final Completion)	27-Aug-2021			↑
Close Out Start	30-Aug-2021			↑
Close Out Finish	12-Oct-2021			↑


↑ Ontime/Early

↓ Delayed/ Late

## PROGRESS SUMMARY

Feb 22, 2022: Project continues, installation and construction phase is 98% complete.

## BUDGET/COST STATUS

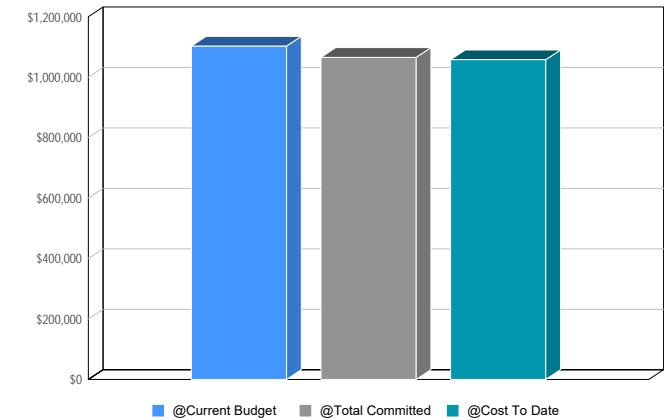

## FINANCIAL STATUS

	BUDGET		COMMITMENT				EXPENDITURE		
	A	B	C	D=B+C	E	F=D+E	G=A-F	H	I=H/A
	Current Budget	Commitments	Approved Changes	Total Committed	Pending Changes	Projected Costs	Estimate To Complete	Cost To Date	% Expended
01. Soft Cost	135,030	137,793	0	137,793	0	137,793	-2,763	134,285	99.45%
02. Hard Cost	429,697	439,697	-50,000	389,697	0	389,697	40,000	389,697	90.69%
03. FF&E	538,152	537,086	1,066	538,152	0	538,152	0	533,757	99.18%
04. Project Contingency	0	0	0	0	0	0	0	0	0.00%
<b>Total:</b>	<b>1,102,878</b>	<b>1,114,576</b>	<b>-48,934</b>	<b>1,065,641</b>	<b>0</b>	<b>1,065,641</b>	<b>37,237</b>	<b>1,057,738</b>	<b>95.91%</b>
